Kennedy Middle School August 14, 2017

School Committee

Kennedy Middle School

August 14, 2017

Approved Building Location Zone 3

BROWN SCHOOL

WETLAND


WETLAND

KENNEDY SCHOOL

STUDY ZONE 3 ISOLATED WETLANDs

NORTH

35.2 acres

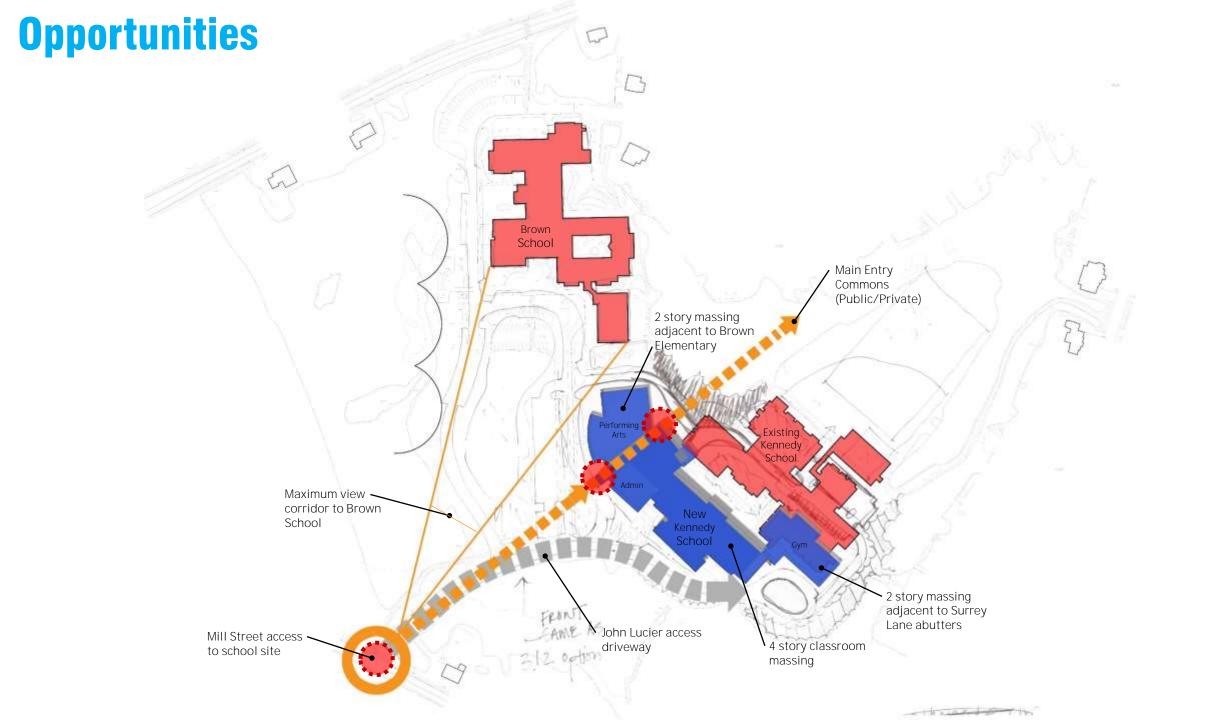

New School Option








Mar 2019 Jan 2021

Phase I


- March 2019: Contractor Mobilization
- January 2021: Substantial completion of 2-story performing arts and 4-story academic core
- *February 2021*: School move-in during February vacation

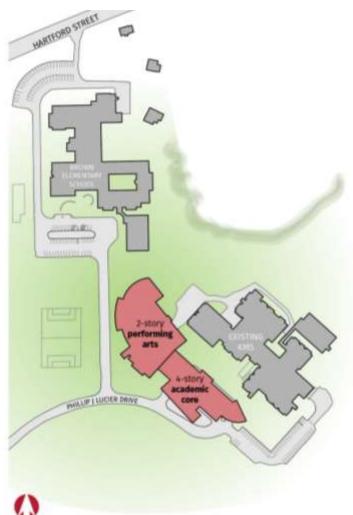



Phase II

- January 2021: Begin abatement and demolition of existing building; sequence from southeast corner (nearest library media center and kitchen) to northwest corner (existing gymnasium to remain)
- March 2021: Begin construction of 2-story athletic center
- June 2021: Begin construction of new athletic fields, including synthetic turf field
- August 2021: Substantial completion of athletic center and synthetic turf fields; abatement and demolition of existing gym complete

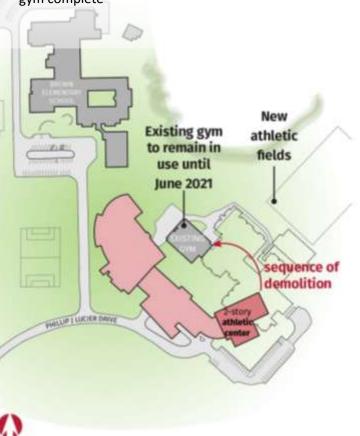




Phase III


- **August 2021**: Begin final site work at former middle school building location
- *April 2022*: Complete site work




Floor Plans


7/24/17: Building Committee Presentation

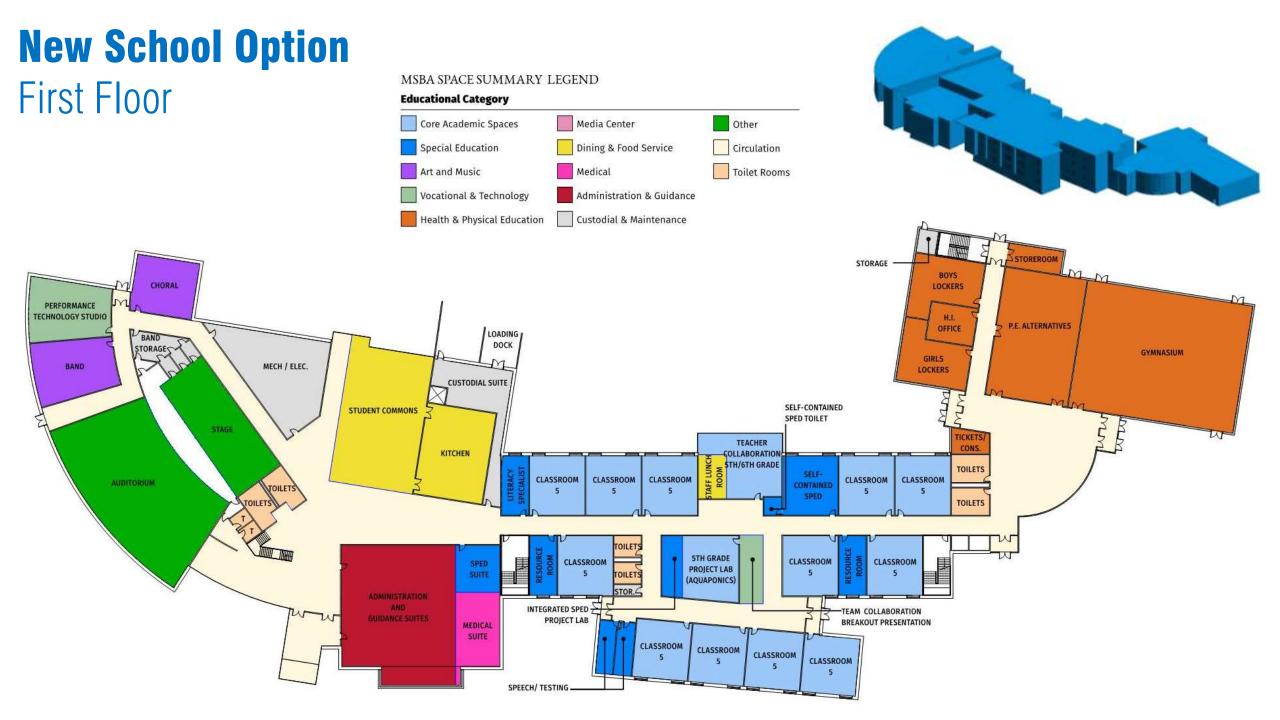

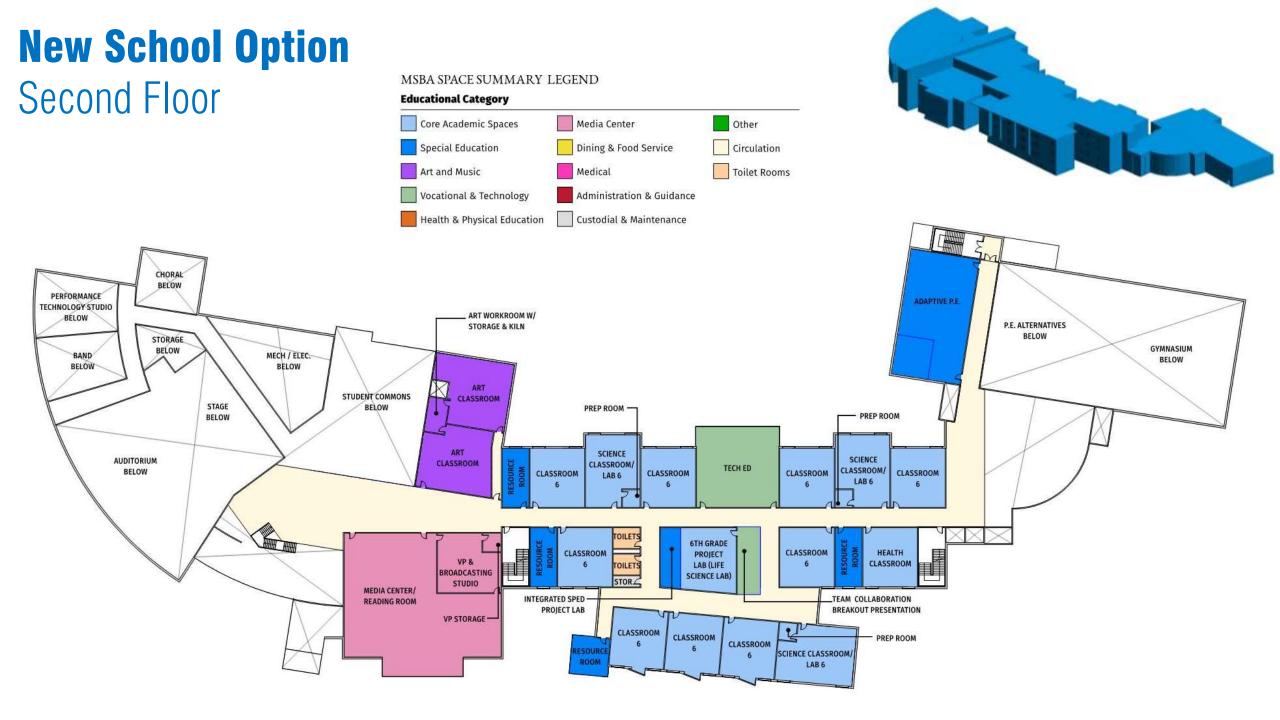


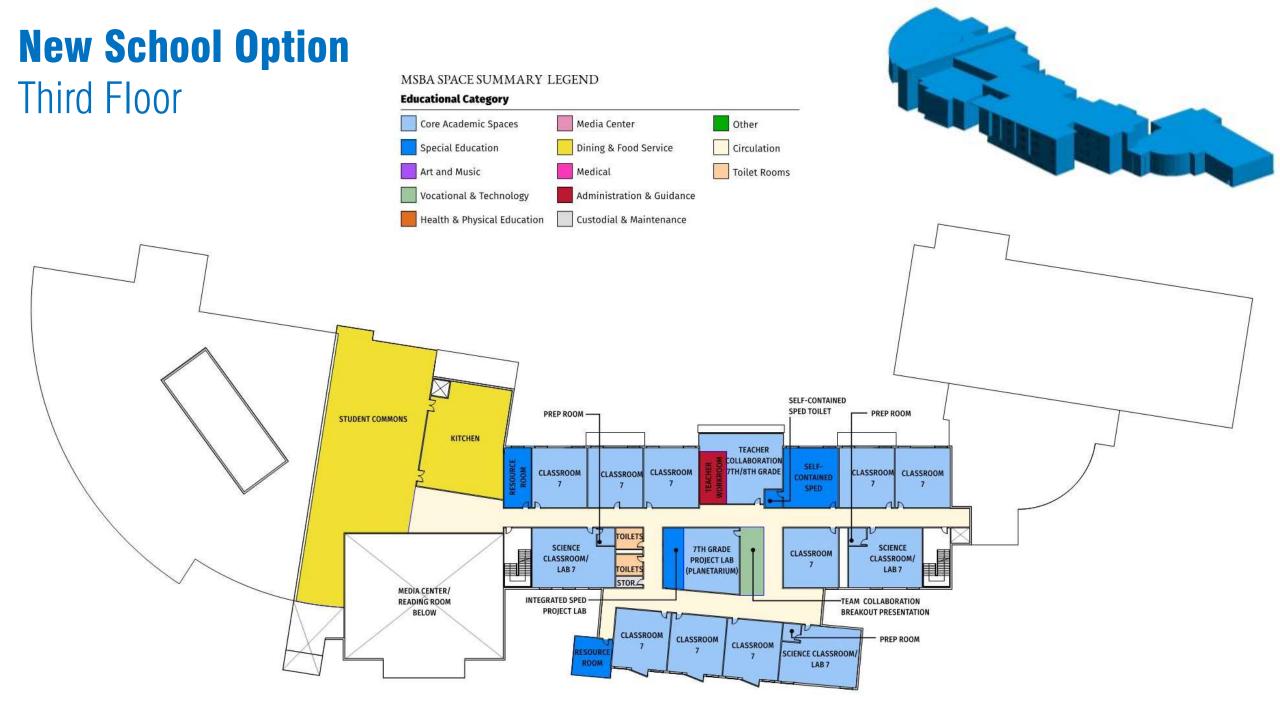


New School Option Fourth Floor



MSBA SPACE SUMMARY LEGEND





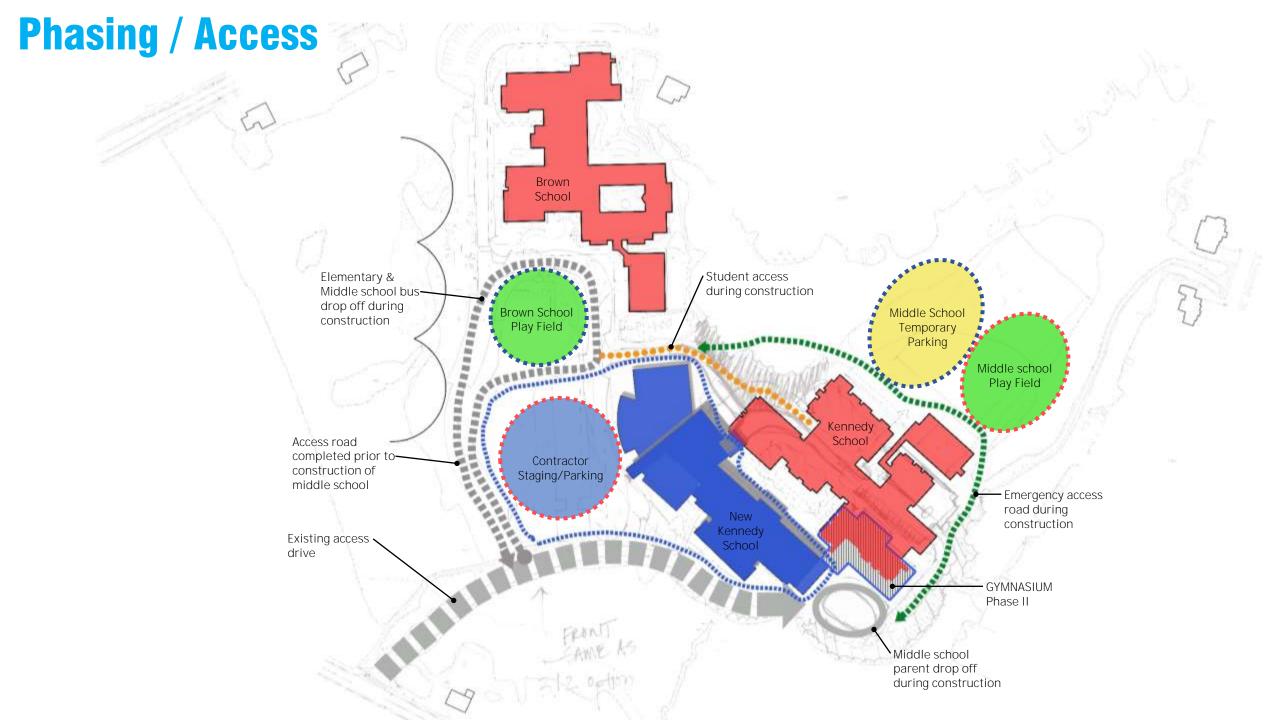

Questions
